ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1						
2		Select House Lot	1 day	Thu 6/1/23	Thu 6/1/23	
3		Select house plan	1 day	Fri 6/2/23	Fri 6/2/23	2
4		Survey/Engineering	1 day	Mon 7/10/23	Mon 7/10/23	3
5		Building Permit	1 day	Tue 7/11/23	Tue 7/11/23	3,4
6		Lot Clearing	1 day	Tue 7/11/23	Tue 7/11/23	4
7		Excavation	1 day	Wed 7/12/23	Wed 7/12/23	6
8		Underground utilities	1 day	Thu 7/13/23	Thu 7/13/23	7
9		Underground plumbing	2 days	Fri 7/14/23	Mon 7/17/23	8
10		Foundation	2 days	Fri 8/11/23	Mon 8/14/23	8,9
11		Concrete floor slab	1 day	Tue 8/15/23	Tue 8/15/23	10
12		Rough backfill	1 day	Wed 8/16/23	Wed 8/16/23	11
13		Framing, TJI, sub-floor, sheeting	15 days	Thu 8/17/23	Wed 9/6/23	10,11,12
14		Trusses	1 day	Thu 9/7/23	Thu 9/7/23	13
15		Roof Sheeting	1 day	Fri 9/8/23	Fri 9/8/23	14
16		Shingles	2 days	Mon 9/11/23	Tue 9/12/23	15
17		Exterior doors and Windows	2 days	Wed 9/13/23	Thu 9/14/23	16
18		Garage door	1 day	Mon 9/11/23	Mon 9/11/23	15
19		Siding	5 days	Fri 9/15/23	Thu 9/21/23	18,17
20		Porch and back deck	2 days	Fri 9/22/23	Mon 9/25/23	19
21		Framing Inspection	0 days	Fri 9/8/23	Fri 9/8/23	15
22		Rough plumbing	2 days	Fri 9/15/23	Mon 9/18/23	23
23		Rough HVAC	2 days	Wed 9/13/23	Thu 9/14/23	16
24		Rough Electrical	3 days	Tue 9/19/23	Thu 9/21/23	22
25		Mechanical Inspections	0 days	Thu 9/14/23	Thu 9/14/23	23
26		Insulation, walls	2 days	Fri 9/15/23	Mon 9/18/23	25
27		Dry wall	10 days	Tue 9/26/23	Mon 10/9/23	26,20
28		Plaster	5 days	Tue 10/10/23	Mon 10/16/23	27
29		Prime and paint	2 days	Tue 10/17/23	Wed 10/18/23	28
30		Cabinets	3 days	Thu 10/19/23	Mon 10/23/23	29
31		Flooring (vinyl T&G)	3 days	Tue 10/24/23	Thu 10/26/23	29,30
32		Interior doors	2 days	Fri 10/27/23	Mon 10/30/23	31
33		Interior trim	5 days	Tue 10/31/23	Mon 11/6/23	32
34		Countertops, built on site	3 days	Tue 11/7/23	Thu 11/9/23	33
35		Finish HVAC	1 day	Thu 10/19/23	Thu 10/19/23	29
36		Finish plumbing	3 days	Fri 11/10/23	Tue 11/14/23	34

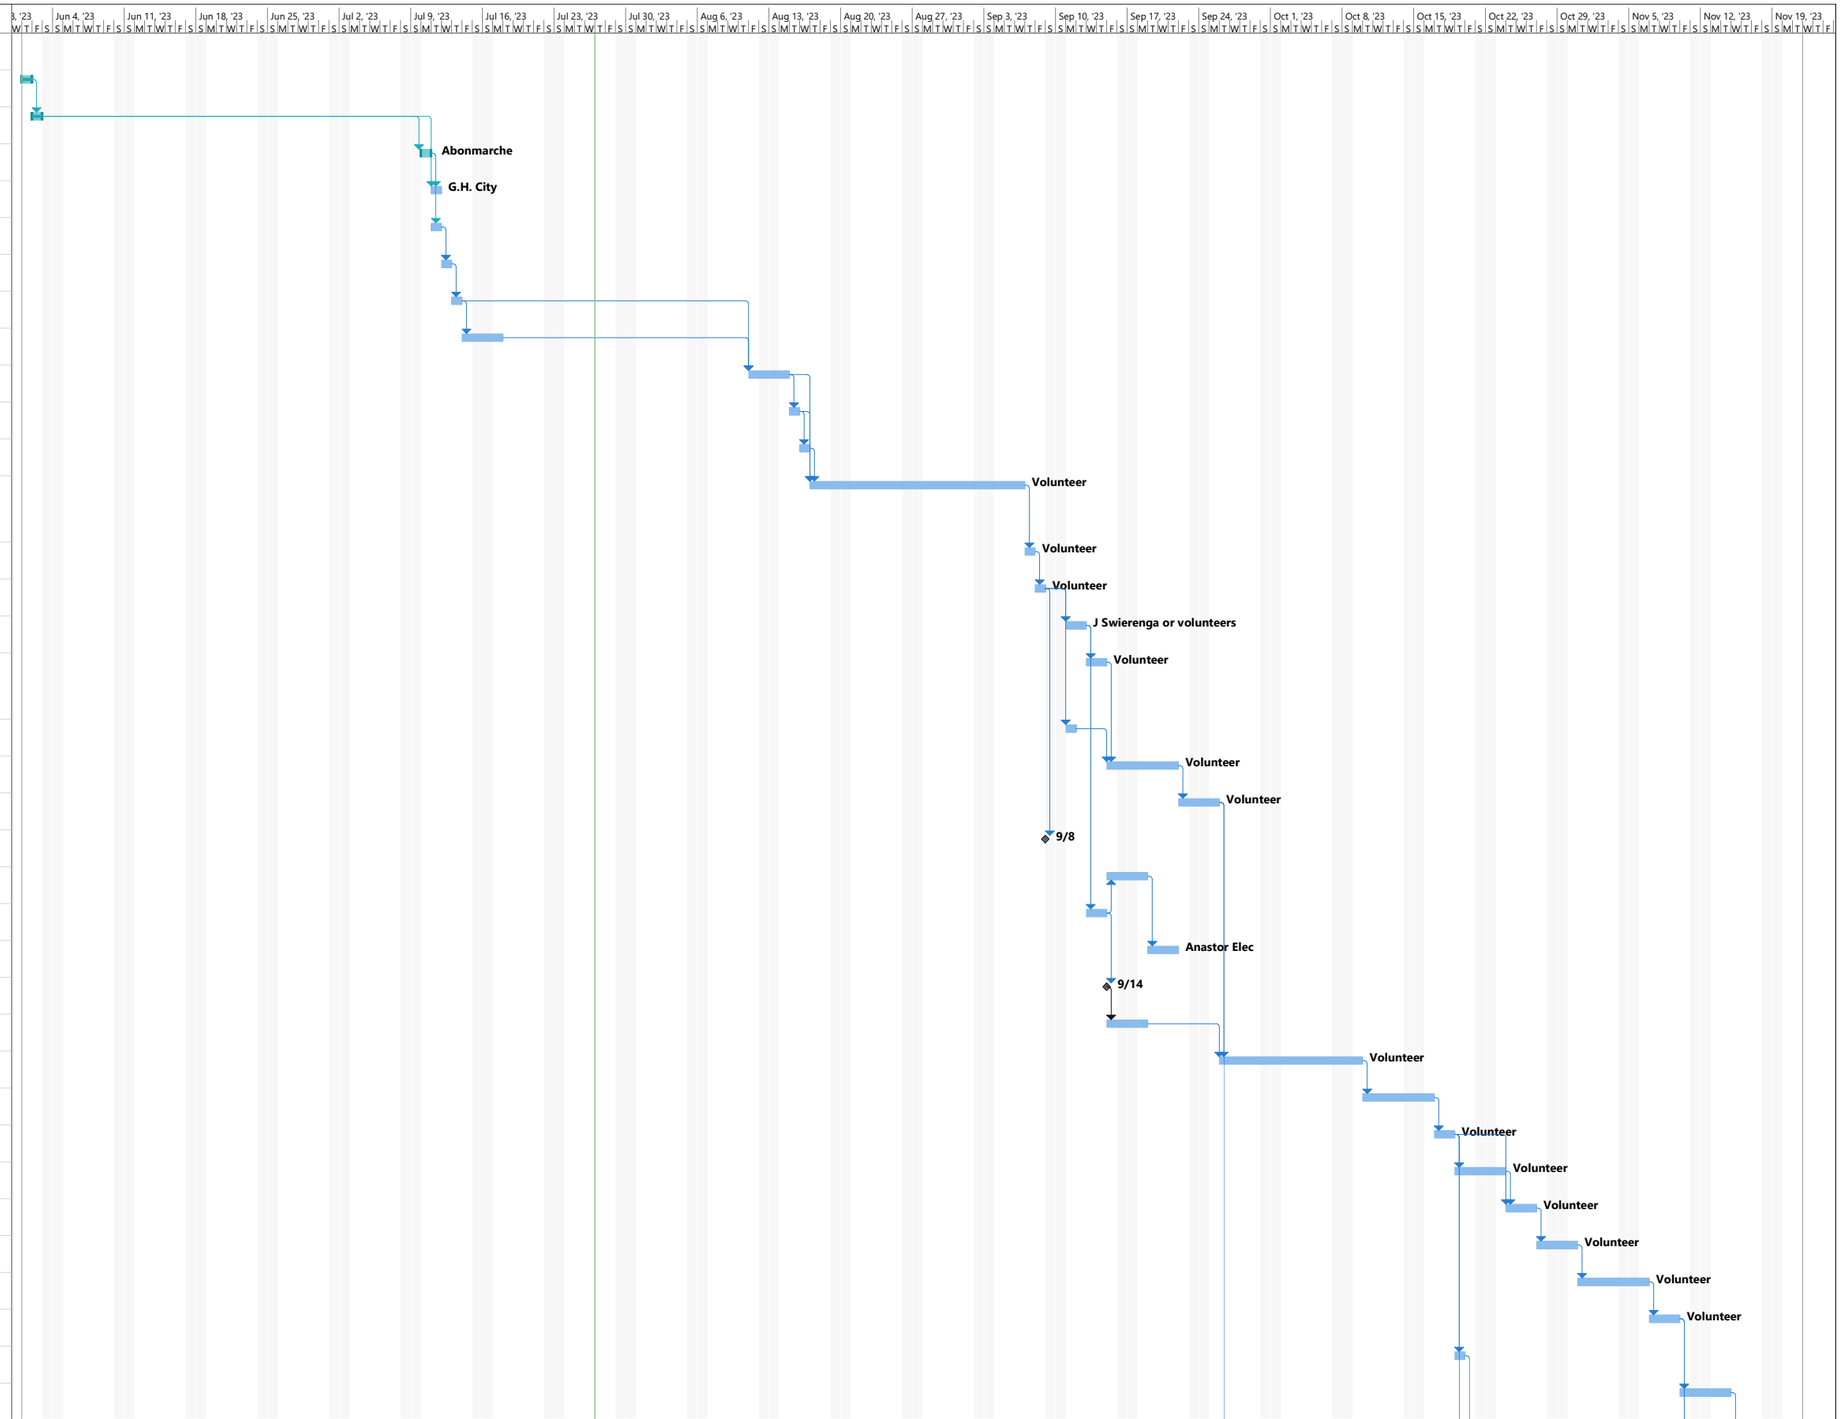

Project: HfH Despleder home
Date: Thu 7/27/23

Task | Milestone | Project Summary | Inactive Milestone | Manual Task | Manual Summary Rollup | Start-only | External Tasks | Deadline | Manual Progress
Split | Summary | Inactive Task | Inactive Summary | Duration-only | Manual Summary | Finish-only | External Milestone | Progress

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors
37			Finish Electrical	2 days	Thu 10/19/23	Fri 10/20/23	29
38			Finish Grade	1 day	Tue 9/26/23	Tue 9/26/23	20
39			Concrete Sidewalk, drive, approach	1 day	Wed 9/27/23	Wed 9/27/23	38
40			landscape	5 days	Fri 11/10/23	Thu 11/16/23	34
41			Blower test	1 day	Mon 10/23/23	Mon 10/23/23	37
42			Cleanup	1 day	Fri 11/17/23	Fri 11/17/23	40
43			Electric final inspection	0 days	Fri 10/20/23	Fri 10/20/23	37
44			HVAC final inspection	0 days	Thu 10/19/23	Thu 10/19/23	35
45			Plumbing final inspection	0 days	Tue 11/14/23	Tue 11/14/23	36
46			Building final inspection	1 day	Mon 11/20/23	Mon 11/20/23	45,42
47			Occupency permit	1 day	Tue 11/21/23	Tue 11/21/23	46

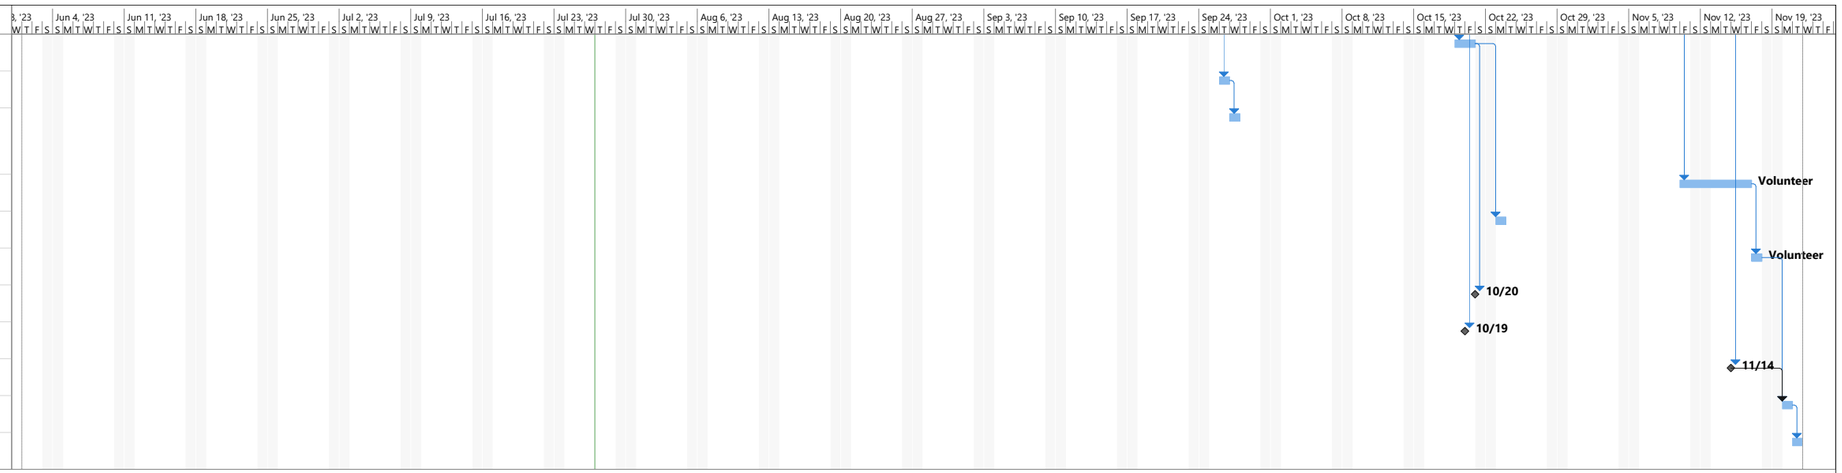

Project: HfH Despleder home
Date: Thu 7/27/23

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
